


Activity ID	Activity Name	Activity Type	Original Duration	Start	Finish	2022				2023			
						Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar

52206 Tarpon Ave.						171	Aug-19-22	Apr-14-23
A1000	NTP	Task Depend	0	Aug-19-22	Aug-19-22			
A1010	Submittals Review	Task Depend	10	Aug-19-22	Sep-01-22			
A1020	Call In Locates	Task Depend	4	Aug-19-22	Aug-24-22			
A1030	Utilities Meeting/Coordination	Task Depend	4	Aug-25-22	Aug-30-22			
52206.Phase 1 Traffic Running Inside Lanes Only						98	Aug-31-22	Jan-13-23
A1050	Advance Warning Intallation	Task Depend	10	Aug-31-22	Sep-13-22			
A1060	Mobilization	Task Depend	0	Sep-14-22	Sep-14-22			
A1070	Traffic Shifted To Inside Lanes	Task Depend	1	Sep-14-22	Sep-14-22			
A1080	Soft Dig For Strain Poles	Task Depend	2	Sep-15-22	Sep-16-22			
A1090	Demo 103+34LT to 104+89 LT	Task Depend	5	Sep-19-22	Sep-23-22			
A1100	Install Strain Poles	Task Depend	2	Sep-26-22	Sep-27-22			
A1110	Excavate And Stabalize 103+34LT to 104+89LT	Task Depend	5	Sep-28-22	Oct-04-22			
A1120	Pour Curb 103+34LT to 104+89 LT	Task Depend	2	Oct-05-22	Oct-06-22			
A1130	Pour Sidewalk 103+34LT to 104+89 LT	Task Depend	2	Oct-07-22	Oct-10-22			
A1140	Demo 103+23RT to 104+86RT	Task Depend	5	Oct-11-22	Oct-17-22			
A1150	Excavate And Stabalize 103+23RT to 104+86RT	Task Depend	5	Oct-18-22	Oct-24-22			
A1160	Pour Curb 103+23 RT to 104+86 RT	Task Depend	2	Oct-25-22	Oct-26-22			
A1170	Pour Sidewalk And Driveways 103+23 RT to 104+86 RT	Task Depend	2	Oct-27-22	Oct-28-22			
A1180	Direction Drill Conduit At Tarpon Mall	Task Depend	3	Oct-31-22	Nov-02-22			
A1181	Install Pull And Splice Boxes	Task Depend	4	Nov-03-22	Nov-08-22			
A1190	Demo 106+30RT to 107+87RT	Task Depend	5	Nov-09-22	Nov-15-22			
A1200	Insttall Excavate And Stabalize 106+30RT to 107+87RT	Task Depend	1	Nov-16-22	Nov-16-22			
A1210	Pour Curb, Sidewalk, And Driveways 106+30RT to 107+87RT	Task Depend	4	Nov-17-22	Nov-22-22			
A1220	Demo And Pour 4 Ramps At Tarpon Mall Instersection	Task Depend	5	Nov-23-22	Nov-29-22			
A1230	Demo 110+71RT to 111+41RT	Task Depend	3	Nov-30-22	Dec-02-22			
A1240	Pour Curb, Driveway, and Sidewalk 110+71RT to 111+41RT	Task Depend	2	Dec-05-22	Dec-06-22			
A1250	Demo 112+06RT to 112+49RT	Task Depend	1	Dec-07-22	Dec-07-22			
A1260	Pour Curb And Sidewalk 112+06RT to 112+49RT	Task Depend	2	Dec-08-22	Dec-09-22			
A1261	Install Pedestrian Poles	Task Depend	4	Dec-12-22	Dec-15-22			
A1270	Pull Span Wire, Hang Lights, Inspected And Tested	Task Depend	5	Dec-16-22	Dec-22-22			
A1280	Grade And Sod	Task Depend	5	Dec-23-22	Dec-29-22			
A1290	Pave Widening 103+20RT to 104+86RT	Task Depend	10	Dec-30-22	Jan-12-23			
A1320	Temporary Striping For Lane Traffice Shift	Task Depend	1	Jan-13-23	Jan-13-23			
52206.Phase 2 Traffic Running Outside Lanes Only						65	Jan-16-23	Apr-14-23
A1300	Switch Traffic To Outside Lanes	Task Depend	1	Jan-16-23	Jan-16-23			
A1310	Mil And Prep For Concrete Seperator	Task Depend	3	Jan-17-23	Jan-19-23			
A1330	Demo Seperator 109+70LT to 111+94LT	Task Depend	3	Jan-20-23	Jan-24-23			
A1340	Pour New Concrete Seperator	Task Depend	8	Jan-25-23	Feb-03-23			
A1341	Intall Delineators And Post Mounted Signs	Task Depend	2	Feb-06-23	Feb-07-23			
A1350	Switch Lights To New Install And Remove Old	Task Depend	2	Feb-08-23	Feb-09-23			
A1360	Demo 112+76LT to 114+75LT	Task Depend	5	Feb-10-23	Feb-16-23			
A1370	Pour Curb	Task Depend	3	Feb-17-23	Feb-21-23			
A1380	Install Sod	Task Depend	4	Feb-22-23	Feb-27-23			
A1390	Mill and Pave	Task Depend	5	Feb-28-23	Mar-06-23			
A1391	Install Loop Detection Systems	Task Depend	2	Mar-07-23	Mar-08-23			

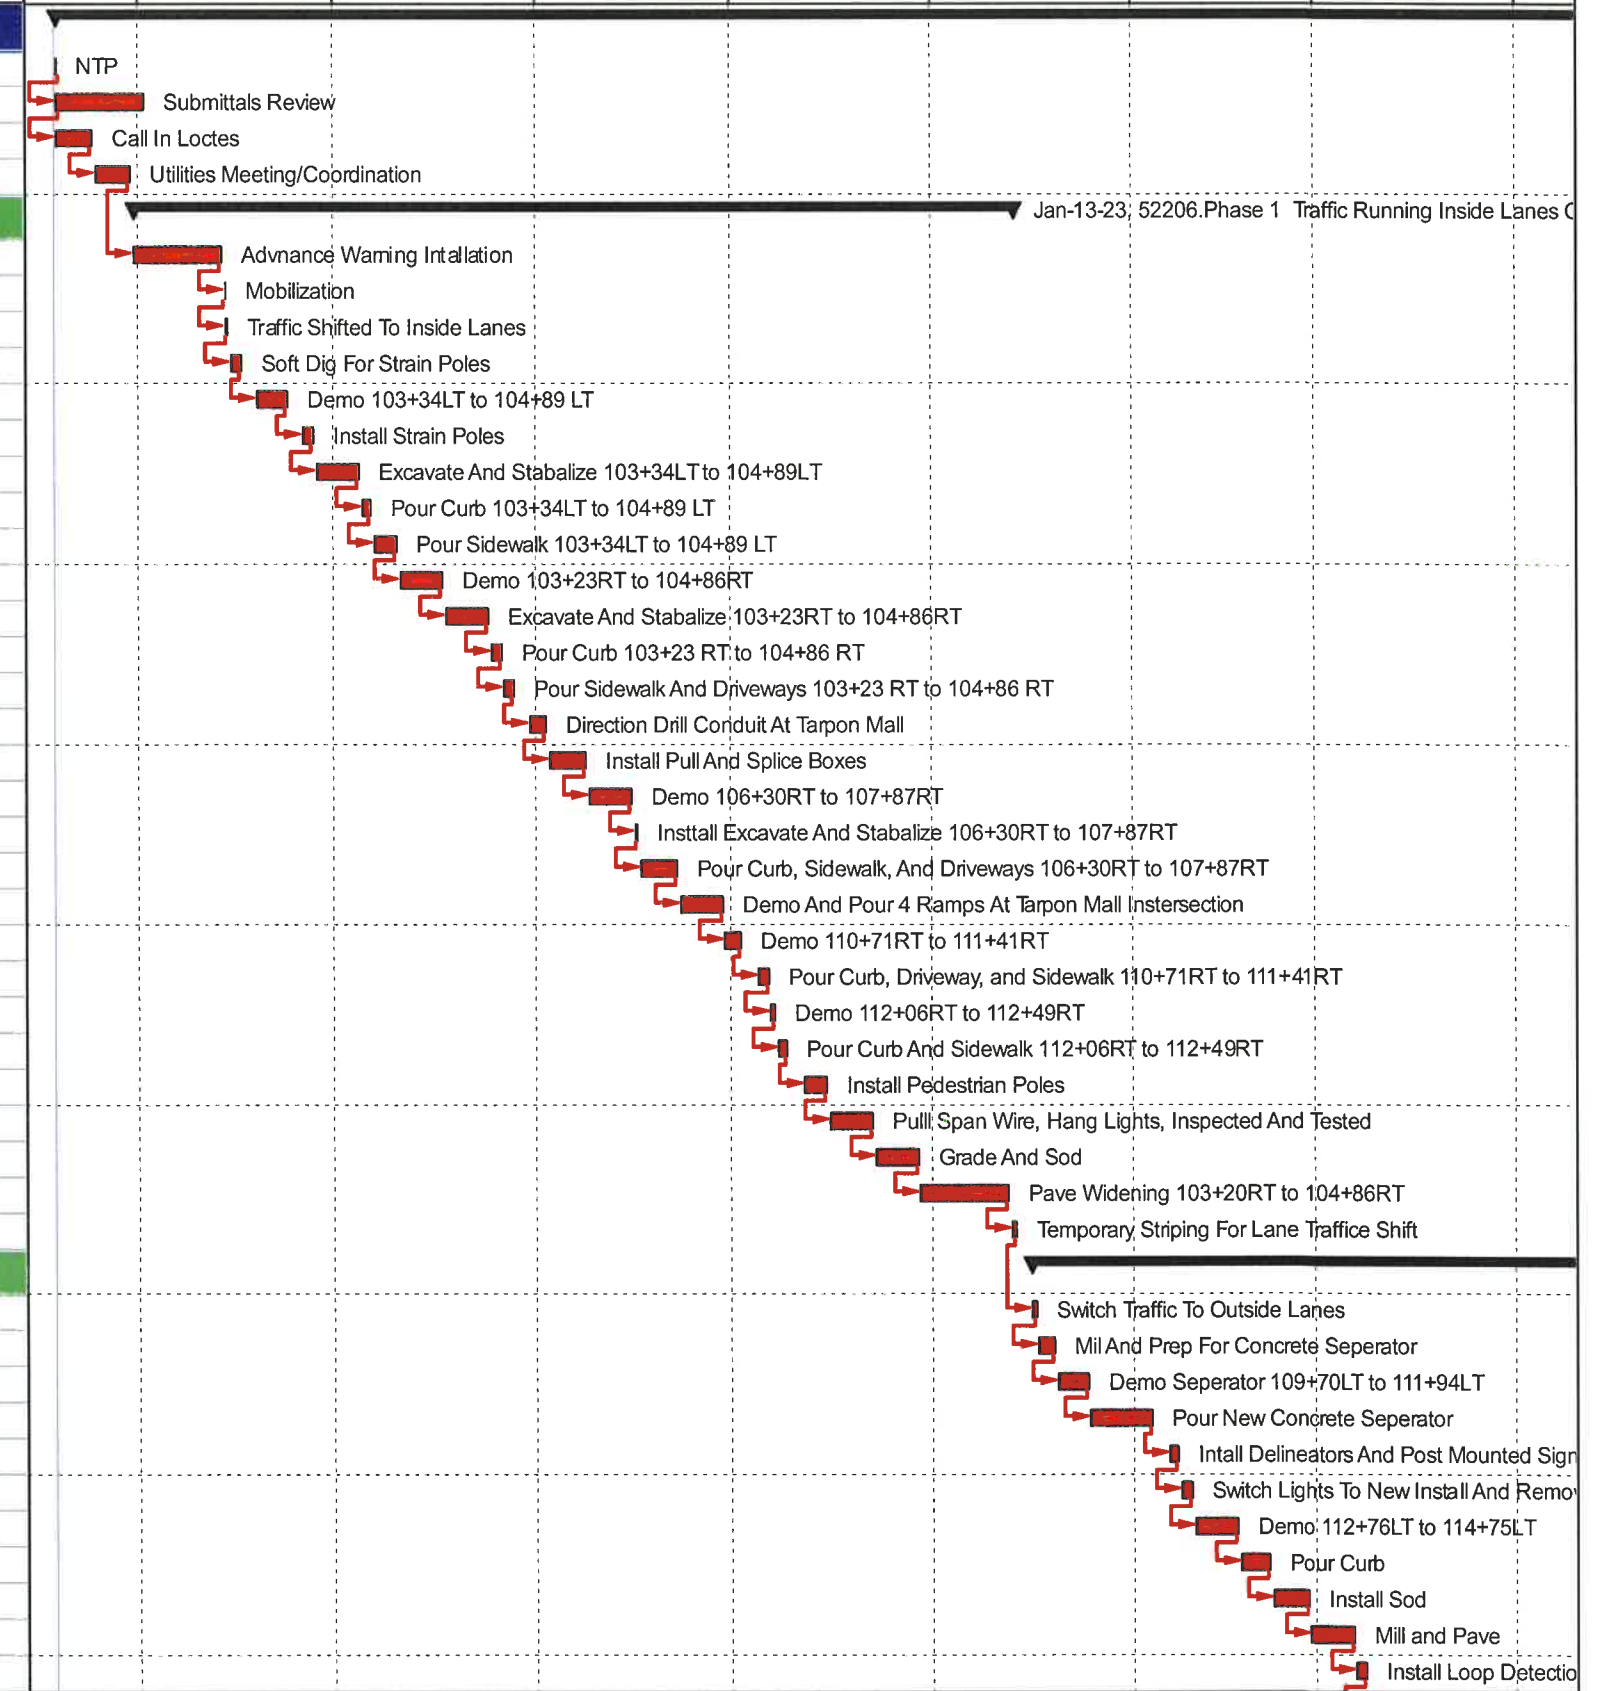

█ Actual Level of Effort
 █ Remaining Work
 ◆ Milestone
 █ Critical Remaining Work
 ▼ summary

Tarpon Ave.			Anthony 1st				Aug-18-22 14:17							
Activity ID	Activity Name	Activity Type	Original Duration	Start	Finish	, 2022		Qtr 4, 2022			Qtr 1, 2023		2023	
						Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr
A1400	Temp to Perm Striping	Task Depend	1	Mar-09-23	Mar-09-23								Temp to Perm Stripi	
A1410	Project Clean Up	Task Depend	2	Mar-10-23	Mar-13-23								Project Clean Up	
A1420	Walkthrough	Task Depend	1	Mar-14-23	Mar-14-23								Walkthrough	
A1421	Puch List	Task Depend	5	Mar-15-23	Mar-21-23								Puch List	
A1430	Thermo Striping	Task Depend	4	Mar-22-23	Mar-27-23								Thermc	
A1440	Project Closeout	Task Depend	14	Mar-28-23	Apr-14-23									

