

CITY OF TARPON SPRINGS, FLORIDA
Development Services Department

EROSION CONTROL AFFIDAVIT

Building Permit No. _____ - _____

I (we), _____ the undersigned certify that I (we) am (are) the
Print or Type Name(s)
owner(s) or duly appointed agent for the property described below.

Project Address

Street Address	Lot	Block
Subdivision	Parcel No.	

I (we) certify that all soil erosion control methods including silt fence and tree protection will be installed and inspected by the City of Tarpon Springs prior to calling for the first building type inspection. Please see the Tarpon Springs Code of Ordinances for more information. A copy of the approved details for silt fence installation and tree protection fence barriers can be found on our website.

Applications & Forms

<https://www.ctsfl.us/building-development-applications-and-forms/>

Tarpon Springs Code of Ordinances

https://library.municode.com/fl/tarpon_springs/codes/code_of_ordinances?nodeId=CITASPFL

Owner/Agent Signature

Date

Co-Owner Signature

Date

CITY OF TARPON SPRINGS, FLORIDA
Building Development Department
STORMWATER MANAGEMENT FACILITY CERTIFICATION

Please print or type

Project Name		
Address	Lot	Block
Subdivision	Permit No.	

Please check appropriate response:

Project/Land Description:

- _____ Residential – Less than 1 acre
- _____ Commercial/Industrial Less than 1 acre
- _____ Residential – More than 1 acre but less than 5 acres (Requires: CGP/ERP)
- _____ Residential – Greater than 5 acres (Requires: CGP/ERP)
- _____ Commercial/Industrial-Greater than 1 acre. (Requires: CGP/ERP)

Storm Management Program Utilized:

- _____ City of Tarpon Springs Minimum Specifications
- _____ Submitted Plan (approved by City staff)
- _____ Plan submitted and approved on Site Plan

I, the undersigned understand the STORMWATER MANAGEMENT PROGRAM required to be instituted and hereby certify that all facets of said plan shall be utilized during all phases of construction. I further certify that the developer for whom I represent shall be held liable for any deviations of said STORMWATER MANAGEMENT PLAN, and will be subject to any and all fines and/or imprisonment that may be imposed as a result of non-compliance of said STORMWATER MANAGEMENT PLAN.


Signature

Date

PERMITEE INFORMATION


Name		
License No.		
Company Name		
Company Address		
City	State	Zip
Telephone No.		

STANDARD SILT FENCE (18" HIGH)



JOINING FENCE SECTIONS

*STAKES SPACED @ 8' MAX.
USE 2"x2" ($\pm \frac{3}{8}$ ") WOOD
OR EQUIVALENT STEEL (U
OR T) STAKES.

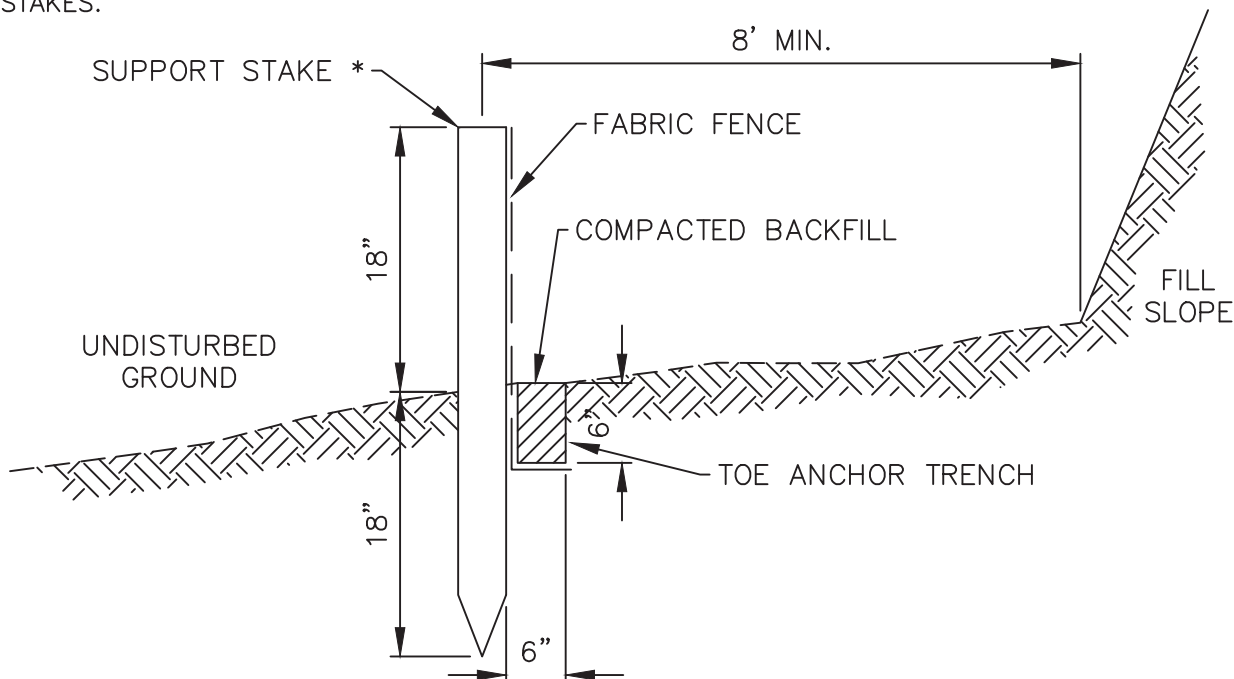

FABRIC WIDTH SHALL BE 30" MINIMUM. STAKES SHALL BE HARDWOOD OR EQUIVALENT STEEL (U OR T) STAKES.

SILT FENCE SHALL BE PLACED AT LEVEL EXISTING GRADE. BOTH ENDS OF THE FENCE SHALL BE EXTENDED AT LEAST 8 FEET UP SLOPE AT 45 DEGREES TO THE MAIN FENCE ALIGNMENT.

SEDIMENT SHALL BE REMOVED WHEN ACCUMULATIONS REACH HALF THE ABOVE GROUND HEIGHT OF THE FENCE.

ANY SECTION OF SILT FENCE WHICH HAS BEEN UNDERMINED OR TOPPED SHALL BE IMMEDIATELY REPLACED WITH A ROCK FILTER.

FENCE SHALL BE REMOVED AND PROPERLY DISPOSED OF WHEN TRIBUTARY AREA IS PERMANENTLY STABILIZED.

USER: [Steven.Torres] Date: [May 27, 2016] Time: [2:45pm] File Location: [\\AED-SERVER\Shared Folders\CADD\Municipal\Tarpon Springs\14.TS-25 (Standards Update)\Cadd\Current\G-01.dwg]






**CITY OF
TARPON SPRINGS**
PINELLAS COUNTY, FLORIDA

SILT FENCE INSTALLATION DETAIL

DATE	12/15/15
INDEX	G-01
SCALE	SHEET
N.T.S.	1 OF 1

USER: [Steven.Torres] Date: [May 27, 2016] Time: [2:45pm] File Location: [\\AED-SERVER\Shared Folders\CADD\Municipal\Tarpon Springs\14.TS-25 (Standards Update)\Cadd\Current\G-02.dwg]

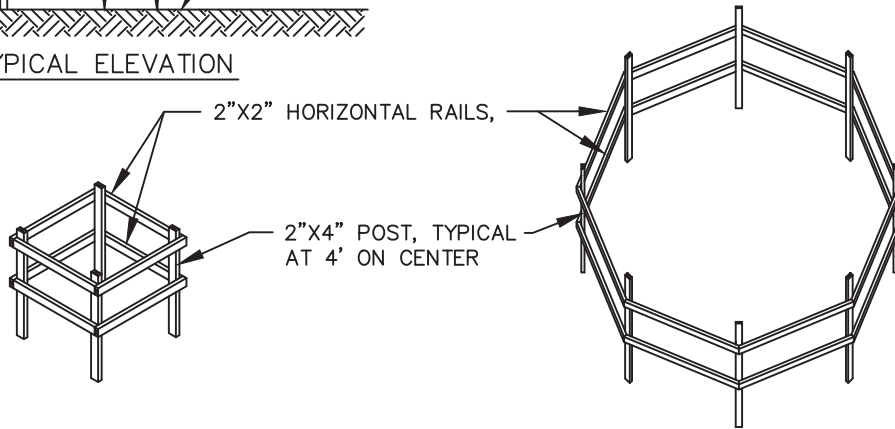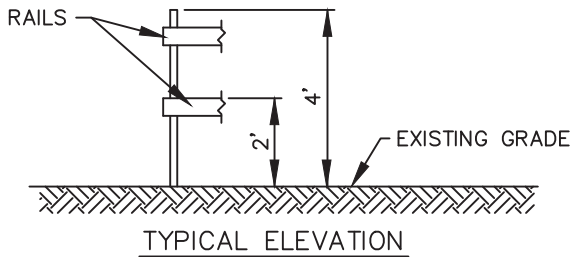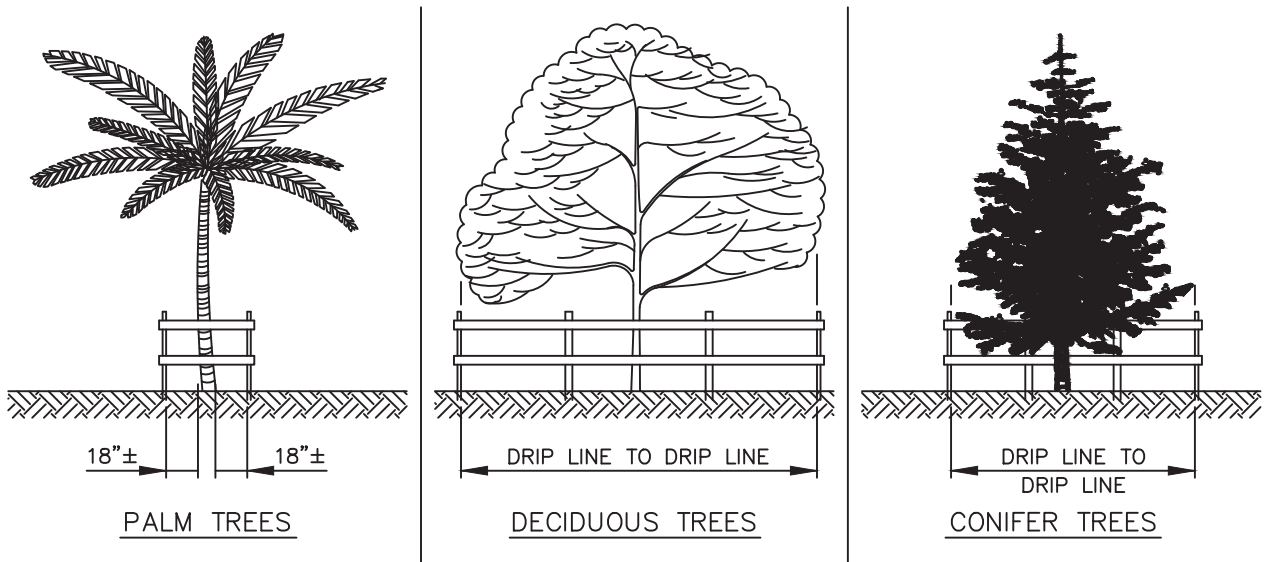

PALMS AND SMALL TREES
SEE NOTE 5

LARGE TREES AND TREE CLUSTERS
SEE NOTE 6

NOTES:

1. NO TRUCKS OR HEAVY EQUIPMENT ALLOWED WITHIN BARRIERS, ONLY HAND LABOR ALLOWED.
2. NO CONSTRUCTION MATERIALS, SOIL DEPOSITS, OR SOLVENTS SHALL BE ALLOWED INSIDE BARRIERS.
3. BARRIERS ARE TO BE IN PLACE PRIOR TO ANY CONSTRUCTION ACTIVITIES NEAR TREES.
4. BARRIERS ARE TO REMAIN IN PLACE UNTIL ALL PAVING, CONSTRUCTION, AND HEAVY EQUIPMENT ARE REMOVED FROM THE AREA.
5. FOR SINGULAR PALM TREES AND TREES FROM 1" TO 8" DBH.
6. FOR LARGER TREES LARGER THAN 8" DBH AND TREE CLUSTERS THAT NEED BARRIERS.



**CITY OF
TARPON SPRINGS**
PINELLAS COUNTY, FLORIDA

**TREE PROTECTION FENCE
BARRIERS DETAIL**

DATE	12/15/15
INDEX	G-02
SCALE	SHEET
N.T.S.	1 OF 1

FERTILIZATION REQUIREMENTS

TREES, PALMS, SHRUBS, AND GROUND COVER:

ALL TREES, PALMS, SHRUBS, AND GROUND COVER SHALL BE FERTILIZED WITH "AGRIFORM" OR APPROVED EQUAL OF 20-15-5 TABLETS AT THE TIME OF INSTALLATION AND PRIOR TO COMPLETION OF PIT BACK-FILLING. THE TABLETS SHALL BE PLACED UNIFORMLY AROUND THE ROOT MASS AT A DEPTH THAT IS BETWEEN THE MIDDLE AND BOTTOM OF THE ROOT MASS.

APPLICATION RATE:

TREES:	3 - 21 GRAM TABLETS PER EACH 1/2" OF CALIPER
PALMS:	1 - 21 GRAM TABLETS PER EACH 1" OF CALIPER
1 GALLON CONTAINER:	1 - 21 GRAM TABLETS
3 GALLON CONTAINER:	2 - 21 GRAM TABLETS
5 GALLON CONTAINER:	3 - 21 GRAM TABLETS
7 GALLON CONTAINER:	4 - 21 GRAM TABLETS
15 GALLON CONTAINER:	7 - 21 GRAM TABLETS

GROUND COVER AREAS:

ALL GROUND COVER AREAS SHALL RECEIVE FERTILIZATION WITH "OZMOCOTE" OR APPROVED EQUAL, TIME RELEASE FERTILIZER AS PER THE MANUFACTURER'S RECOMMENDATIONS.

WATERING SCHEDULE

THE 52 WEEK ESTABLISHMENT WATERING SCHEDULE SHALL BE AS FOLLOWS:

WEEKS 1 AND 2	6 TIMES PER WEEK
WEEKS 3 THRU 5	5 TIMES PER WEEK
WEEKS 6 THRU 11	4 TIMES PER WEEK
WEEKS 12 THRU 17	3 TIMES PER WEEK
WEEKS 18 THRU 25	2 TIME PER WEEK
WEEKS 25 THRU 52	1 TIME EVERY OTHER WEEK, MIN. OR AS NEEDED TO INSURE THE SURVIVABILITY OF THE TREES, PALMS, SHRUBS AND GROUND COVER THROUGHOUT THE WARRANTY PERIOD
TREES:	20 GALLONS EACH
PALMS:	20 GALLONS EACH
SHRUBS:	3 GALLONS EACH
GROUND COVER:	2 GALLONS PER PLANTING

WARRANTY PERIOD

TREES:	ONE YEAR FROM DATE OF FINAL ACCEPTANCE
PALMS:	ONE YEAR FROM DATE OF FINAL ACCEPTANCE
SHRUBS:	120 DAYS FROM THE DATE OF FINAL ACCEPTANCE
GROUND COVER:	120 DAYS FROM THE DATE OF FINAL ACCEPTANCE



**CITY OF
TARPON SPRINGS**
PINELLAS COUNTY, FLORIDA

**FERTILIZATION, WATERING AND
WARRANTY DETAIL**

DATE	12/15/15
INDEX	G-03
SCALE	SHEET
N.T.S.	1 OF 1
